

One governed CMS platform for ONE

Replace 27 Drupal instances to simplify publishing, deliver changes faster and reduce long-term maintenance.

Switch to one CMS to simplify work and lower cost

Recommendation: evaluate Payload as ONE's shared CMS. Technical detail begins on Slide 20.

01 Faster engineering decisions

One shared backlog, common standards and reusable changes across countries.

02 Simpler publishing

One editor portal, Google SSO, drafts, preview and planned releases.

03 Lower long-term effort

Maintain one platform and reuse improvements across all 27 site scopes.

04 A practical path to switching

Sales call → four-sprint proof of concept (POC) → implementation order.

The POC will test workflow fit and migration, and document recurring CMS costs before implementation is ordered.

Start with a Payload sales call and an eight-week POC

A proof of concept (POC) is a bounded test of whether Payload fits ONE's real operating needs.

1 • CALL PAYLOAD SALES

Confirm Enterprise scope, support, trial access, roadmap and pricing.

3 • DECIDE WHETHER TO PROCEED WITH IMPLEMENTATION

Proceed only after the POC evidence, total CMS cost and delivery capacity are accepted.

2 • RUN THE POC

Eight people complete four two-week sprints against agreed evidence gates.

DECISION BOUNDARY

The sales call and POC do not approve a licence purchase or implementation.

Expected direction: lower CMS running cost and maintenance effort, with more consistent publishing.

Twenty-seven Drupal stacks repeat cost and maintenance

27

Drupal instances

26 country sites and one global site.

Repeated platform work Patches, releases, regression tests and support are repeated across separate stacks.

Fragmented operations Content, configuration and reporting sit across isolated databases and hosting boundaries.

Separate editing destinations Editors managing several sites switch between Drupal domains and site-specific settings.

Engineering: reuse improvements across countries. Editors: one place to draft, preview and publish.

One platform connects decisions, delivery and publishing

CURRENT

27 separate CMS stacks

Repeated hosting, upgrades, testing and support across country and global instances.



PROPOSED

One shared CMS and editor portal

Centralize engineering priorities and releases. Keep country content ownership and access.

One place to decide

Shared backlog and technical standards

One place to improve

Reusable features, fixes and integrations

One place to edit

Country and global content with clear roles

Centralize the platform while preserving each country's control over its content.

Decide once, build once, improve every site

Shorter path from request to release

One shared backlog and clear technical ownership simplify prioritization, approvals and delivery.

Less development work over time

Reuse page blocks, forms and integrations across countries. Extend a common solution for the next request.

Less repeated maintenance

Share fixes, upgrades, tests and release tooling across the platform. Reduce separate configurations to maintain.

More predictable changes

Use the same engineering standards, Google SSO and release process for CMS and website changes.

Example: improve a shared news template once, then release it to the countries that use it.

Give editors one place to work, preview and publish

One portal + Google SSO

Manage authorized country and global content in one place, without switching between 27 Drupal domains.

Drafts + autosave

Prepare changes while the published page stays live. Save work as editors write.

Live Preview

Check how a page will look on the website before publishing it.

Version history + trash bin

Review earlier edits, restore a previous version, and recover content moved to trash.

Scheduled publishing

Prepare a release in advance. Schedule when content goes live or returns to draft.

Google SSO is proven. Payload supports the editing tools above; ONE will enable them for the agreed content types and roles.

Make content easier to reuse, review and update

Reusable content and media

Use approved page blocks and assets across authorized sites. Maintain language variants in one editing experience.

Publishing and translation workflows

Give each review, approval and language task a clear owner and status. Validate advanced Enterprise workflows in the POC.

MCP for assisted content work

Connect approved AI tools to find content and help prepare updates. Payload's official MCP server is available; ONE configures access and review.

Future AI-assisted editing

Plan for writing, translation and image assistance as vendor features become available. Keep editors responsible for approval.

Expected value: less copying, fewer review handoffs and more time spent improving content. AI integration and usage are priced separately.

Payload lets ONE build on its existing engineering skills

PREFERRED

Payload

Uses the same TypeScript, React, Next.js and PostgreSQL skills as ONE's website platform.

Shared code and official plugins support reusable forms, country access rules and integrations.

CREDIBLE ALTERNATIVE

Directus

Strong visual data management, workflow automation and configuration-sync capabilities.

Existing internal familiarity remains a relevant advantage.

Both support self-hosting, APIs and access controls. Payload is preferred for its fit with ONE's shared engineering approach.

Payload offers open-source ownership and a roadmap voice

PAYLOAD

MIT open source with Figma backing

The core is MIT open source and self-hostable. Payload joined Figma in June 2025; Enterprise features and support are paid separately.

Roadmap voice: Payload explicitly offers Enterprise customers influence over its roadmap.

Published users: Microsoft, ASICS and Blue Origin.

DIRECTUS

Source available under MSCL

Directus v12 uses MSCL, with GPLv3 conversion after four years. Its free Core tier has limits; ONE needs a commercial scope review.

Roadmap voice: Public feature requests are supported. Confirm Enterprise influence and priority commitments with sales.

Published users: Copa Airlines and Ripley Entertainment.

ONE can retain its code, data and extensions. For either vendor, a roadmap request needs an agreed commitment before it becomes a delivery dependency.

Build on the demo; test ONE's remaining requirements

What we understand

- Google SSO is proven for editors and developers.
- Drafts, autosave and preview are configured in the demo.
- Content and language models fit the website stack.
- Official plugins support multiple sites, forms and MCP.

What the POC will confirm

- ONE's country/global ownership and access rules.
- Advanced publishing and translation workflow fit.
- Representative Drupal imports and business forms.
- Payload Enterprise scope, support and total cost.

Focus the POC on country access, editor workflows and migration using representative ONE content.

Four risks to manage before rollout

Migration complexity

Hidden content, media or form dependencies can delay retirement. Prove sample imports, reconcile each wave and retain rollback until acceptance.

Enterprise fit and cost

Required workflows or terms may not fit. Test the licensed product and obtain a written quote; resolve gaps before ordering.

Country ownership

Unclear shared-content rules can delay approval or expose content. Agree content ownership and access rules with country leads; verify denied access.

Shared-platform outages

One outage can affect all countries. Test restore and rollback, establish incident responsibilities and monitor CMS and public delivery separately.

Persons in charge (PICs) will be agreed later. These proposed responses cover both POC and implementation work.

Allocate eight people for an eight-week POC

Team A runs the POC



The PPO owns the backlog and confirms the flows. The technical architect (TA) owns technical evidence. QA owns testing.

Team B continues current delivery

Its later implementation role requires a separate portfolio decision after the POC.

Before Week 1

Secure Enterprise trial access, representative Drupal data, PPO availability and GCP access.

Eight people: 4 developers, 2 QA, 1 PPO and 1 TA. Prioritize required gates; defer optional exploration. Training starts during implementation.

Four sprints produce reviewable evidence

Weeks 1-2

Agree the test

Confirm use cases and tenant rules. Profile Drupal samples. Verify Enterprise access.

Exit: access matrix and sample agreed

Weeks 5-6

Test platform controls

Test tenant isolation, drafts, extensions and representative load.

Exit: security and quality evidence

Weeks 3-4

Prove content flows

Import news and iframe pages. Test publishing, translation and a representative form.

Exit: import and PPO-confirmed flow evidence

Weeks 7-8

Close the decision

Resolve critical/high defects. Confirm Enterprise scope, total cost and implementation backlog.

Exit: go / no-go and implementation recommendation

Five gates protect the implementation decision

- 1 Use-case coverage** Tenant, publishing, translation and form flows work; PPO confirms them.
- 2 Drupal import** News and iframe samples retain required media and relationships.
- 3 Safe operation** Tenant access, approvals and unpublished content are protected.
- 4 Service readiness** Document the production controls needed to meet ONE's existing service agreement.
- 5 Decision readiness** No open critical/high defects; PPO, TA and QA sign off; Enterprise scope and CMS costs are documented.

If a required capability remains unresolved, choose a clear response: narrow scope, build an extension, extend validation or stop.

Migration follows the POC in controlled waves

Required order: Payload sales call → 8-week POC → evidence review → implementation order → implementation Month 1

Provisional period	Engineering	Content and business
Months 1–3	Platform foundation and integrations	Inventory, cleanup and form decisions
Months 4–6	Pilot launch; begin coexistence	Train pilot editors; user acceptance
Months 7–12	Main page and news migration waves	Review languages; approve each wave
Months 13–15	Remaining iframe content and forms	Accept remaining content and forms
Months 16–18	Final deltas; retire Drupal	Final sign-off and archive approval

The 18-month target starts only after POC acceptance and the implementation order. The fastest consecutive scenario is about 20 months; approval or procurement gaps can extend it.

Total new CMS cost pending Enterprise quote

CURRENT DRUPAL / ACQUIA \$265,000 two-year run rate at the supplied \$132,500 annual subtotal	NEW CMS · ADDED GCP \$12,000–27,600 two-year allowance, before the Enterprise licence	NEW CMS · TOTAL RECURRING COST Pending quote Added GCP + Enterprise licence and support
--	--	--

Baseline to reconcile The supplied Drupal line items do not match its subtotal. Procurement must confirm the contract total.

New CMS total Added GCP infrastructure + Payload Enterprise. Development and AI remain excluded.

USD recurring-cost comparison. Pay for both platforms during migration. Savings depend on Drupal contract retirement. AI and development excluded.

Success means complete migration and practical improvement

Complete retirement	100% of agreed content accepted across all 27 scopes, with no remaining Drupal dependency by implementation Month 18.
Editor readiness	At least 80% of active editors are trained and can complete core publishing tasks.
Publishing efficiency	Aim for 10% less publishing and reviewed-translation time without reducing quality.
Reliable service	At least 97% annual CMS availability including planned downtime, aligned with Unicorn. Recovery must meet the OTS SLA.
Lower operating burden	Lower CMS running cost and maintenance effort than the current Drupal estate.

The improvement targets are proposals, not measured results. Establish comparable Drupal baselines during implementation.

Take the next step toward a simpler CMS platform

1

Call Payload sales

Confirm Enterprise scope, trial, support, roadmap and pricing.

2

Run four POC sprints

Allocate eight people for eight weeks to collect evidence against the five gates.

3

Decide whether to proceed with implementation

Proceed only after evidence, total cost, capacity and backlog are accepted.

Approve the sales call and POC allocation to turn the benefits into a tested implementation decision.

Technical design and validation

The proposed platform fits ONE's current delivery model. The POC must prove the operating details.

01

Architecture and
coexistence

02

Content ownership and
workflow

03

Drupal migration and
cutover

04

Operations, security and
quality

05


Enterprise scope, MCP and
optional AI

Each technical decision remains provisional until the POC or later production testing supplies the required evidence.

Next.js enables controlled CMS coexistence

Coexistence: Next.js serves both CMSs while ownership moves in waves

Pages, news, and forms use the lightest safe migration method; each accepted wave retires its Drupal connection.

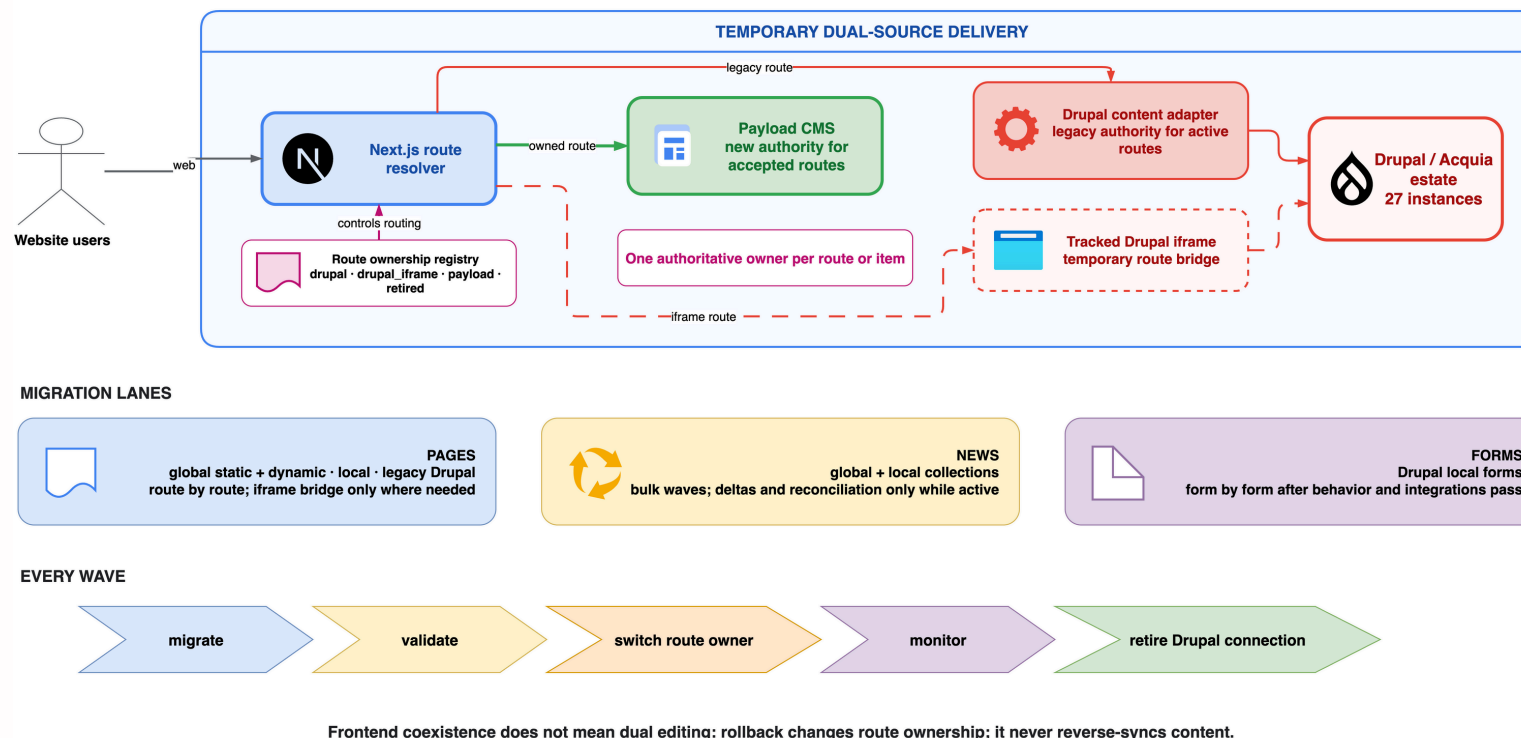


Give each route or item one authoritative CMS. Keep route-level rollback, reconcile final Drupal changes, then retire the accepted wave's Drupal connection.

Payload fits the existing GCP delivery platform

Target: one governed CMS with Enterprise capabilities on GCP

Enterprise AI, MCP, workflow, and audit serve 26 country sites plus one global site from one governed platform.

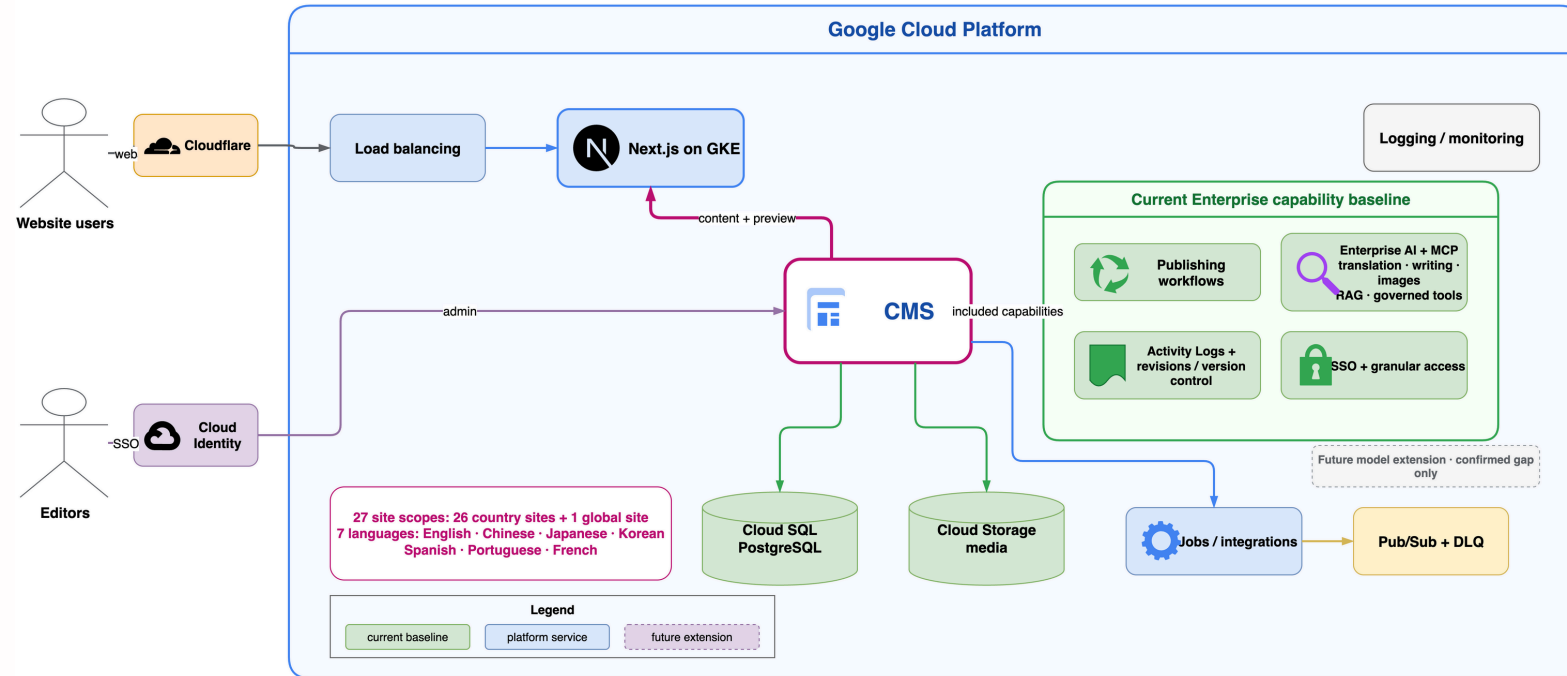

Country ownership and language choice remain independent.

Reuse GKE and Cloudflare; add Cloud SQL and GCS. This is a target design: the diagram's Enterprise AI features remain planned and require release confirmation.

Country ownership and language are separate controls

27

site scopes

One governed codebase using Payload’s multi-tenant foundation.

Seven supported languages

- English
- Chinese
- Japanese
- Korean
- Spanish
- Portuguese
- French

Country or global scope

Defines ownership, access and where content can be used.

Language


Defines which localized variant is written, reviewed and published.

Shared content

Needs explicit source ownership and reuse rules across scopes.

POC question: can multi-tenant support enforce ONE’s ownership and access rules without recreating 27 CMS stacks?

Publishing needs governed workflow and extensibility

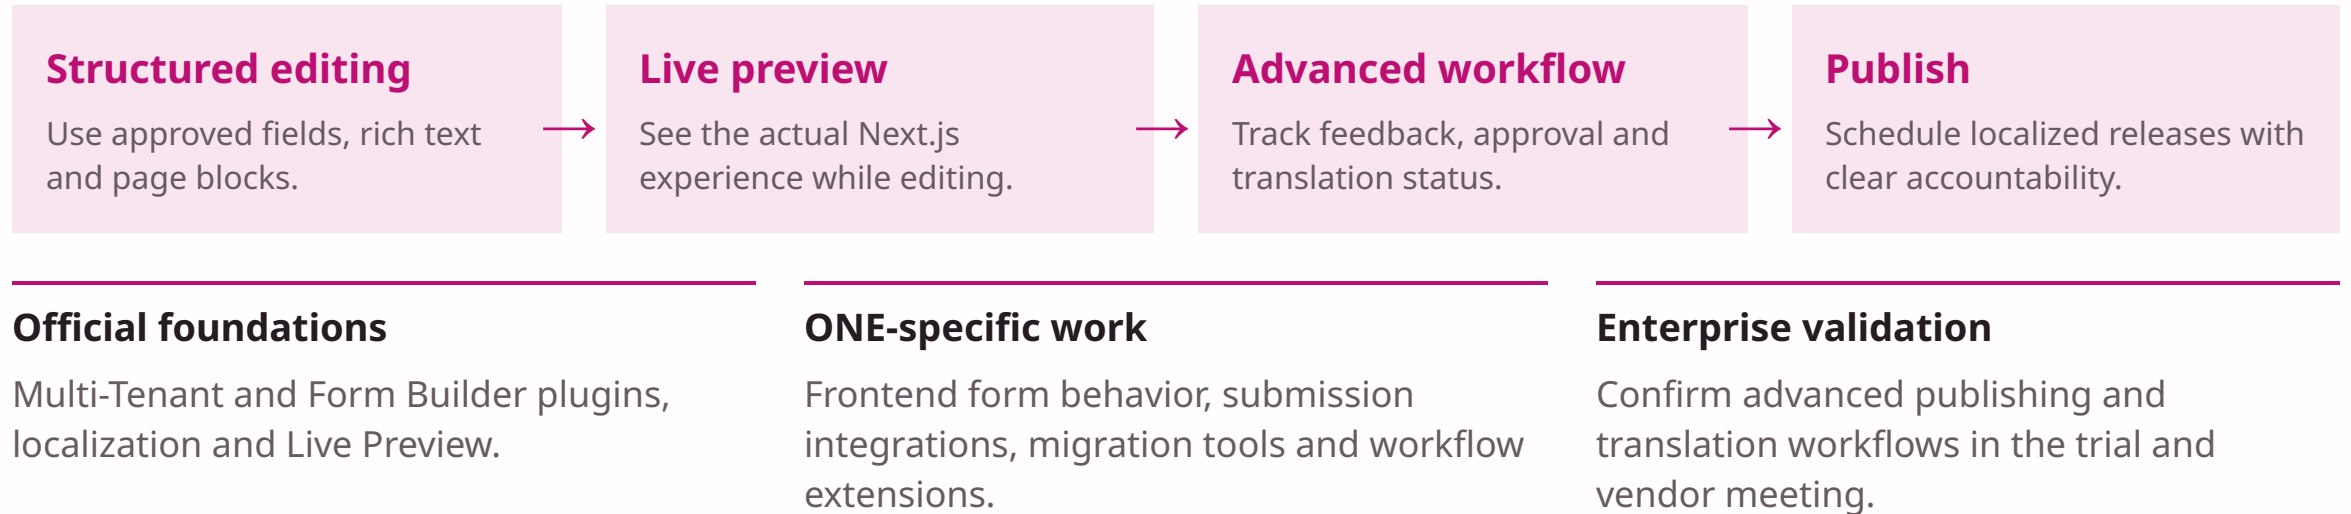

An official plugin is a starting point. It does not prove that every ONE business flow works without extension.

Drupal migration needs repeatable import and cutover rules

Content group	Technical treatment	Acceptance and cutover
Pages	Migrate layouts, content, media and required languages.	Owner accepts each wave, including redirects, links and search visibility.
News	Import dates, media and relationships; support repeatable deltas.	Reconcile final changes before cutover.
Iframe content	Import underlying content/assets and rebuild required behavior.	Remove the Drupal-hosted dependency.
Forms	Migrate, rebuild or centralize each approved form destination.	Validate consent, submission, routing and retention.

One authoritative CMS per route or item. Keep rollback during validation; remove Drupal only after acceptance.

Production readiness needs clear service controls

Deployment	GKE deployment is established; define environment ownership and release controls.
Data	Own PostgreSQL in Cloud SQL and media in a dedicated GCS bucket.
Capacity	Measure real traffic and workload; existing shared capacity is not unlimited.
Recovery	Test backup, restore and recovery against the 4.5-hour OTS SLA.
Observability	Track CMS and public delivery health, errors, latency and publish-to-visible freshness.

One shared CMS increases the impact of an outage. Test restore and rollback, assign incident ownership, and verify the production controls.

Security and quality require explicit evidence

Area	Required evidence	When to decide
Tenant and draft isolation	Access tests block unauthorized cross-scope access and public reads of drafts.	POC gate
Critical defects	No open critical/high findings; PPO, TA and QA sign off.	POC gate
Performance	POC records representative load results. Implementation sets and verifies service targets.	POC + implementation
Content freshness	Approved changes appear correctly on the site and in search.	Implementation
Reliability and recovery	Availability is measured separately; recovery meets the OTS SLA.	Implementation + production

Set detailed performance targets from measured workload and capacity. Do not invent thresholds before evidence exists.

MCP is available; AI-assisted editing remains planned

Confirm with Payload

- Enterprise pricing, support terms and trial access.
- Tenant isolation and advanced workflow depth.
- Drupal import, security, service controls and upgrade constraints.
- Environment-promotion options and required extensions.

Plan governed AI assistance

- Use the official MCP server with explicit collection and action permissions.
- Future AI-assisted translation, writing and image tools require release confirmation.
- Do not let AI experiments displace required POC evidence.
- Price AI integration and usage separately from the CMS budget.

Required outputs

Written answers and actions · Enterprise scope and constraints · trial access · licence/support quote or due date

The implementation decision follows evidence. A vendor meeting or successful demo does not commit ONE to purchase or rollout.
